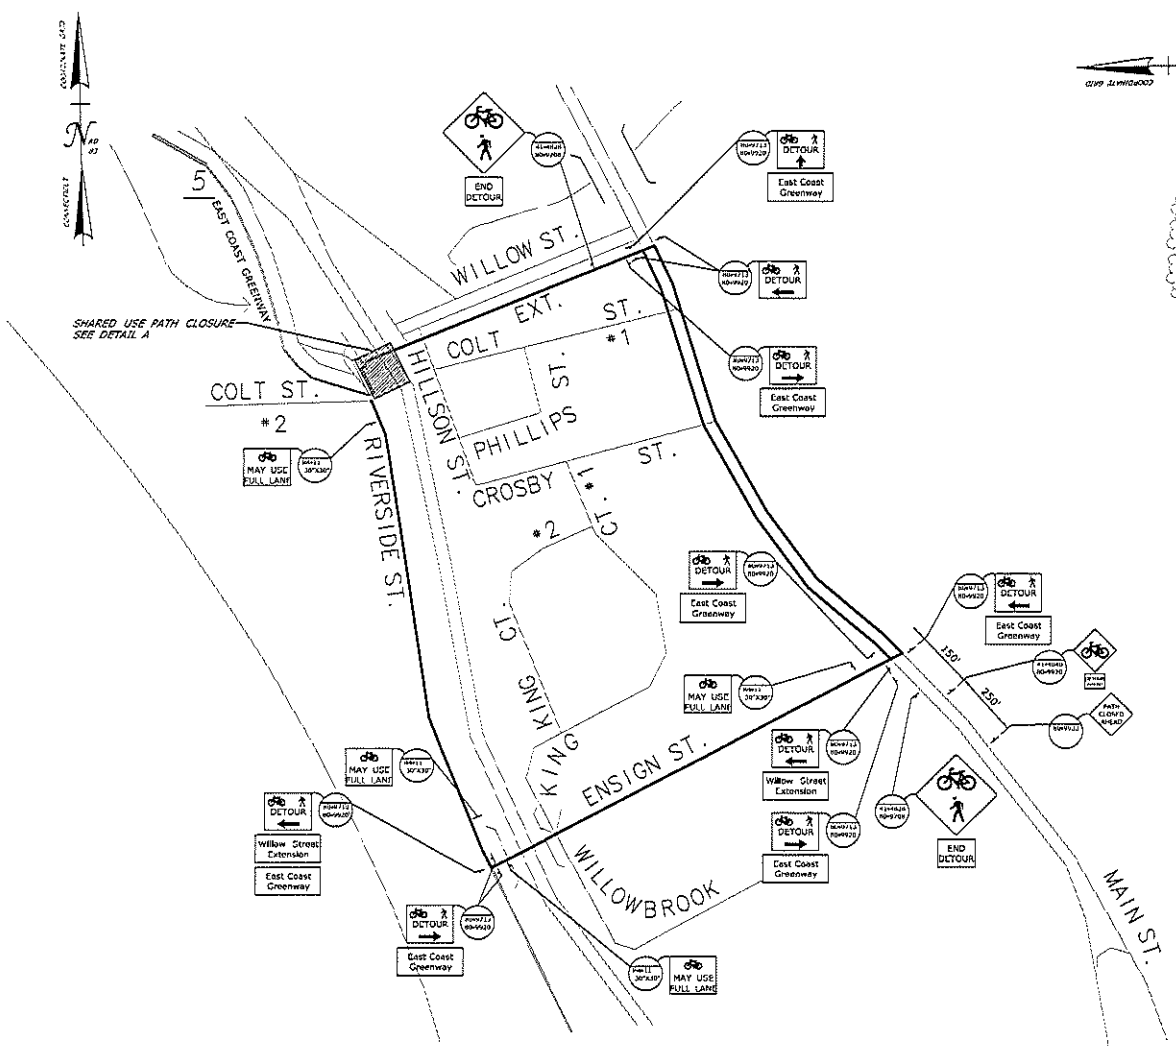

DETOUR PLAN

NOT TO SCALE

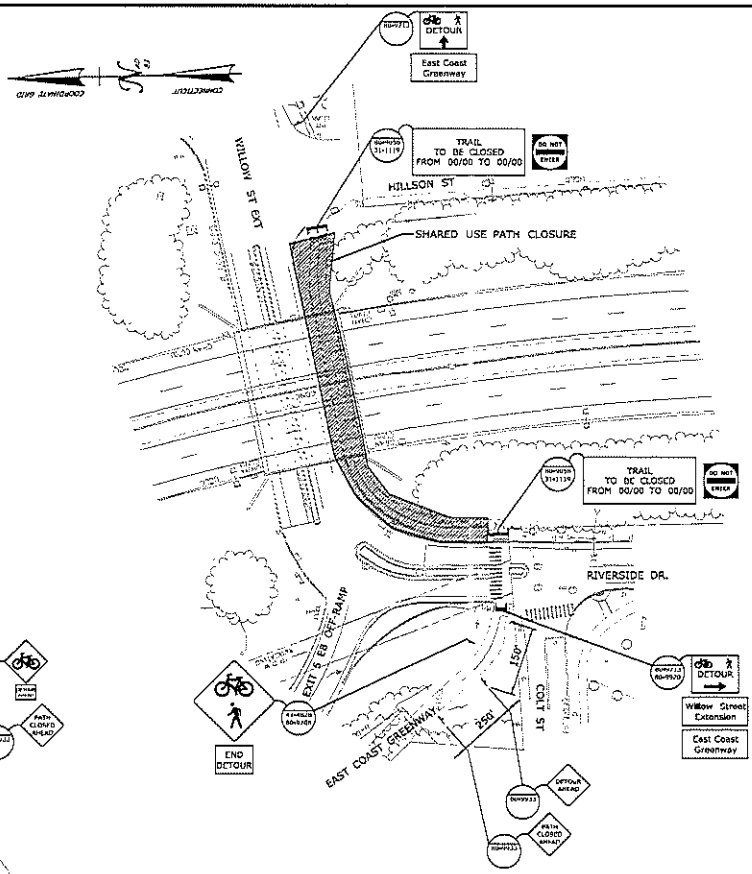

DETAIL A

DETAIL NOT TO SCALE

DETOUR NOTES

1. DETOUR SIGNS ARE TO BE POSTED WHEN DETOUR IS IN EFFECT. DETOUR SIGNS ARE TO BE COVERED OR REMOVED WHEN DETOUR IS NOT IN EFFECT.
2. DETOUR SIGNS ARE PAYABLE UNDER ITEM NO. 1220027: CONSTRUCTION SIGNS.
3. ACCESS AND EGRESS TO ALL STREETS AND DRIVES MUST BE MAINTAINED AT ALL TIMES.
4. EXACT LOCATIONS OF DETOUR SIGNING TO BE VERIFIED IN THE FIELD BY THE ENGINEER.
5. THE CONTRACTOR IS TO NOTIFY DISTRICT 1 CONSTRUCTION, THE DIVISION OF TRAFFIC ENGINEERING, THE TOWN OF EAST HARTFORD, AND GOODWIN UNIVERSITY AT LEAST TWO WEEKS PRIOR TO INITIATING THE DETOUR.
6. INSTALL SIGN NOS. 80-9058 (TRAIL CLOSED) AND 31-1119 (DO NOT ENTER) ON TYPE III CONSTRUCTION BARRICADES.
7. TYPE III CONSTRUCTION BARRICADES ARE TO BE INSTALLED FULLY ACROSS THE PATH.

REV.	DATE	REVISION DESCRIPTION	SHEET NO.

THE INFORMATION, INCLUDING ESTIMATED QUANTITIES OF WORK, SHOWN ON THESE SHEETS IS BASED ON LIMITED INVESTIGATIONS BY THE STATE AND IS IN NO WAY WARRANTED TO INDICATE THE CONDITIONS OF ACTUAL QUANTITIES OF WORK WHICH WILL BE REQUIRED.

Plotted Date: 3/8/2022

DESIGN PERFORMED: WGS
CHECKED BY: RGC
NOT TO SCALE

STATE OF CONNECTICUT
DEPARTMENT OF TRANSPORTATION

SIGNATURE/BLOCK:

PROJECT TITLE: RESURFACING, BRIDGE AND SAFETY IMPROVEMENTS ON ROUTE 2

TOWN: TOWNS OF HARTFORD, EAST HARTFORD, WETHERSFIELD AND GLASTONBURY

DRAWING TITLE: WILLOW ST EXT / GREENWAY DETOUR PLAN

PROJECT NO. 42-317
DRAWING NO. DTR-0X
SHEET NO.
